



Project Status Update


As of October 20th, 2025

NVTA reports monthly the status of projects funded through the Regional Revenue (70%) Fund. Realtime updates can also be found on Novagateway.org

Project Status – Standard Project Agreements (SPAs)

There are a number of projects that received funding for different phases across various funding cycles. This results in the establishment of a SPA (Standard Project Agreement). The stages of a SPA are listed in 5 categories below. While there are a total of 179 SPAs across the different categories, these represent 135 unique projects.

Status: Number of SPAs by Category

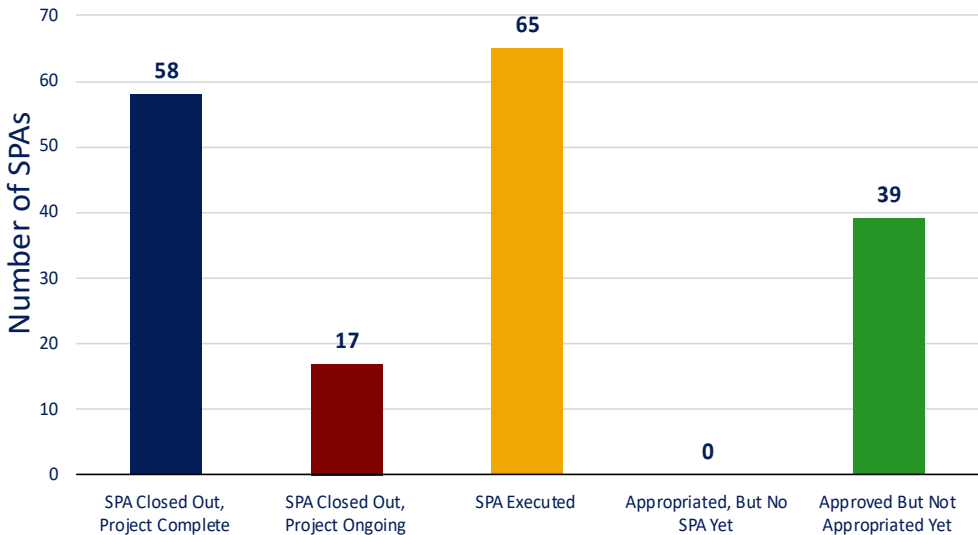

5 Classification Categories and Stages of a SPA

SPA closed out, Project complete: SPA has been closed out and NVTA funding has completed, and overall project has been completed.


SPA closed out, Project ongoing: SPA has been closed out and NVTA funding has completed. Overall project however, is still ongoing.

SPA Executed: SPA has been approved by NVTA.

Appropriated but no SPA yet: Funding allocation has been appropriated by NVTA, but SPA has not been executed yet. (Note: NVTA appropriates the total approved funding amount at time of appropriation)

Approved but not appropriated yet: Project Application approved by NVTA, but funding allocation has not been appropriated yet.


Status: Number of SPAs by Program by Category

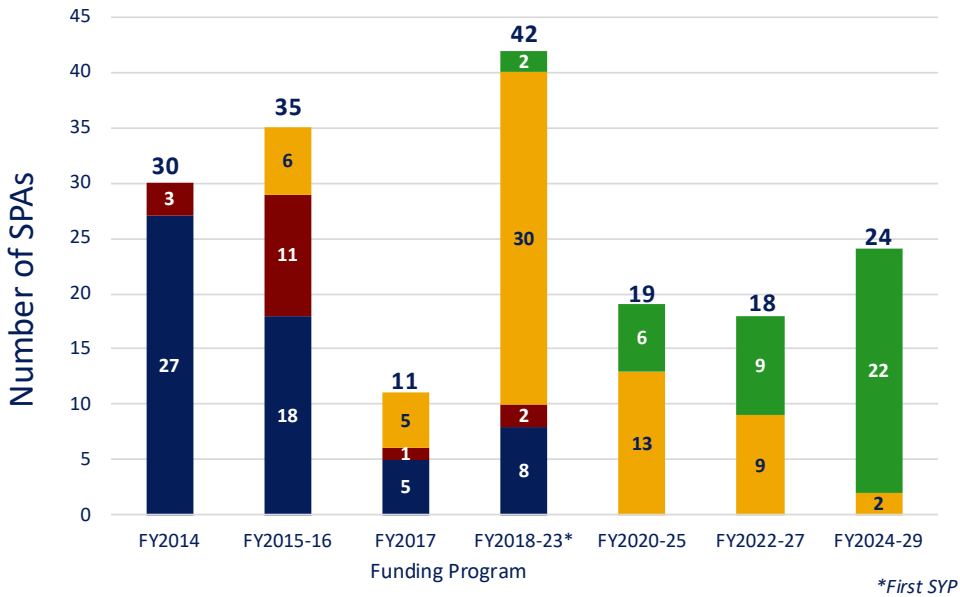


Note: NVTA’s updates to the Six Year Program (SYP) allocate revenues from two future (outer) fiscal years (e.g., the FY2024-2029 SYP allocated funding for FY2028 and FY2029).

Project Status – Revenue Approved, Appropriated and Reimbursed as of October 20th, 2025

NVTA has **approved** a total of: **\$3,683,182,918**
NVTA has **appropriated** a total of: **\$2,416,024,959**
NVTA has **reimbursed** a total of: **\$1,121,153,871**

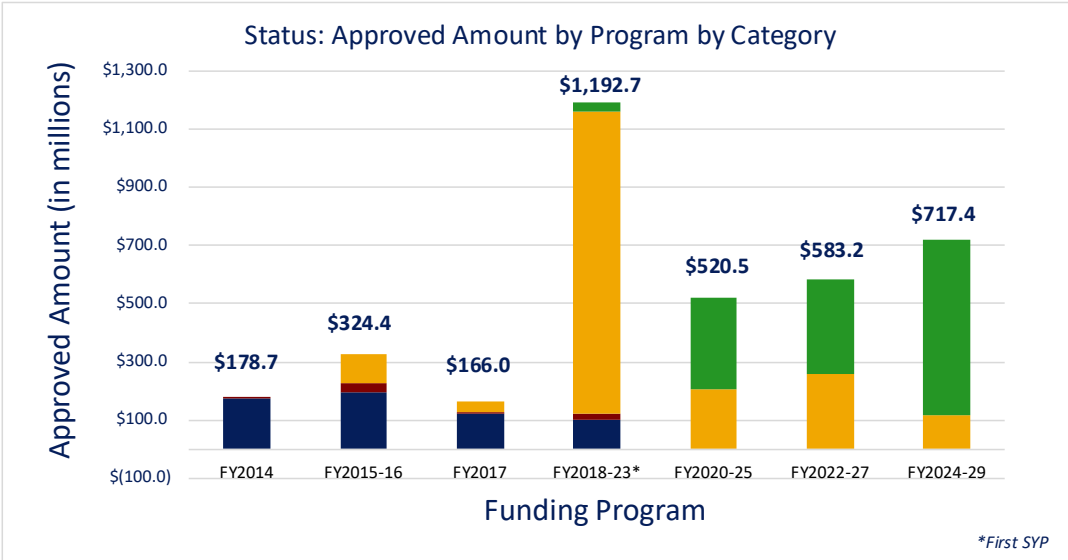

5 Classification Categories and Stages of a SPA
SPA closed out; Project complete
SPA closed out; Project ongoing
SPA Executed
Appropriated but no SPA yet
Approved but not appropriated yet

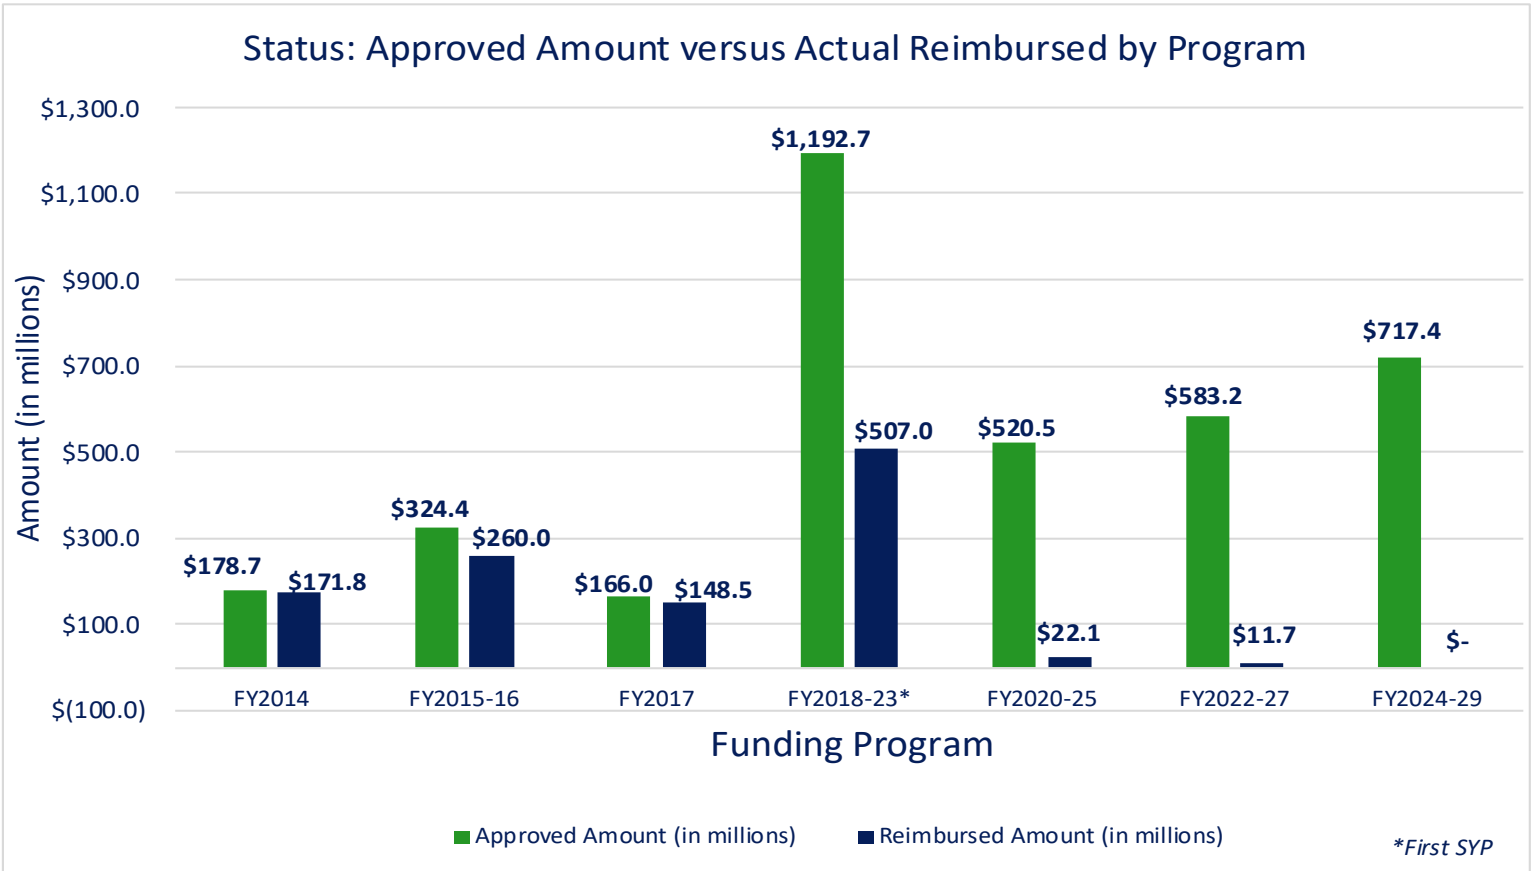

Note: SPAs usually request NVTA funds in the outer years of their approved funding period and then continue to drawdown into subsequent fiscal years. (e.g. SPAs in the FY2024-2029 SYP typically begin drawing funds by the end of FY2029, with most not fully utilizing their allocations until FY2032.)

Recent Project Milestones



VRE Manassas Park Station Parking Expansion

- October 21st Ribbon Cutting event held
- NVTA invested **\$2.5 million in Regional Revenue funds** toward the design of this project
 - Additionally, NVTA recommended **\$23.5 million** to the Commonwealth Transportation Board (CTB) through the I-66 Concessionaire Program toward this project




Arlington County Army Navy Drive

- October 29th Ribbon Cutting event held
- Army Navy Drive is one portion of the overarching Pentagon City Multimodal Connections and Transitway Extension project, in which NVTA invested a total of **\$28.8 million in Regional Revenue funds**
 - In the Army Navy Drive portion, NVTA has invested **\$9.7 million**



Recent Project Milestones *Continued*



Alexandria DASH Facility

- October 30th Groundbreaking event held
- NVTa invested a total of **\$11.9 million in Regional Revenue funds** on this project
 - \$9.2 million toward eight new battery electric buses and \$2.7 million toward construction of the facility



Substantive Project Status Updates

Substantive changes to SPAs for the period September 23rd, 2025- October 20th, 2025, are outlined below.

SPAs Executed

- None

Updated Funding Schedules

- Arlington County:
 - Intelligent Transportation System Improvements (2018-5-1)

SPAs Closed Out

- None



Substantive Project Status Updates *Continued*

Substantive updates reported by the project sponsor for the period of September 23rd, 2025, to October 20th, 2025, are outlined below.

Substantive changes include but are not limited to project administration advancements, start/completion of phases, major engineering progress, project completion date changes, etc.

Project Sponsor	Project Title	Updated Status	% Reimbursed (Program Year(s))
Arlington County	ART Operations and Maintenance Facilities	Project is currently awaiting Dominion Energy to install the transformer & meter for the Battery-electric bus equipment, which remains on back order. Given this, the project completion timeline revised from 6/30/2025 to 3/31/2026.	FY2018: 99%
Arlington County	Columbia Pike Multimodal Street Improvements - East	Utility companies continue to do work for cutover in preparation for the switch from above ground to underground utility service. Completion pushed back one month to 11/31/2025.	FY2015: 91%
Loudoun County	Dulles West Boulevard Widening: Loudoun County Parkway to Northstar Boulevard	Land acquisition and utility relocation activities continue. Land acquisition scheduled to complete December 2025. Construction Notice to Proceed is expected September 2026. Project Completion date pushed from 6/30/2027 to 3/20/2028.	FY2018: 11%
Loudoun County	Northstar Boulevard - Evergreen Mills Rd to Tall Cedars Parkway	Project has achieved substantial completion. The contractor is currently addressing punch list items and is also working on the VDOT street acceptance package.	FY2018: 75%
Loudoun County	Route 15 at Braddock Road Roundabout	After a 9-month hold on the project, Locally Administered Project (LAP) agreement has been completed. Project completion date advanced from 8/17/2031 to 10/31/2029.	FY2024: No SPA yet
City of Fairfax	Jermantown Road/Route 29 Intersection Improvements	Preliminary Design settled. Soil Investigation scheduled.	FY2020: 2%

Substantive Project Status Updates *Continued*

Flagged Projects – as of October 20th , 2025

Projects are flagged when there has been no update or no new information provided for three consecutive months.

Date of Last Update	Jurisdiction	Project Title	NVTA Funds	% Reimbursed
No new update since July 2025. Last update noted “ <i>Pre-construction meeting held 7/17/2025. NTP expected to be issued by end of the month</i> ”	ARL	Crystal City Streets: 12th Street Transitway	\$11,600,000	FY2017: 60%
No new update since June 2025. Last update noted “ <i>Under Active Construction.</i> ”	CFX	Government Center Parkway Extension	\$3,540,000	FY2020: 3%

No Response Received This Cycle

Project sponsors are required to provide monthly updates on projects. NVTA did not receive a monthly update on the projects listed below.

- **Arlington County:** Crystal City Streets: 12th Street Transitway (FY2017), Intelligent Transportation System Improvements (FY2018-23) and Rosslyn Multimodal Network Improvements (FY2020-25)
- **VRE:** Franconia- Springfield Platform Improvements (FY2015), VRE Crystal City Station Improvements (FY2015/FY2018-23/FY2020-25)
